



Nyssa Middle School

Monthly Project Update

November 13, 2017

Summary of Work:

- Sitework is about wrapped up for Fall – still hoping for curb, gutter and ACP at the south lot.
- Structural CMU work is complete. CMU veneer is now underway on the north classroom wing following the fluid applied membrane, rigid insulation and window installation.
- Structural steel stud framing and sheathing is complete and the wood roof structure continues down the south classroom wing. The roof structure will wrap up late this month on the Admin area.
- Roofing has now been completed at the gym and is well underway on the classroom areas – the north wing is dried in and the roofer will continue to follow the framer.
- M, P & E is well underway in the classroom wing and insulation started today. Sheetrock deliveries are expected this week and they'll start hanging GWB as soon as the insulator is inspected.
- M, P & E rough-in work and overhead athletic equipment is complete in the gym and the painter is wrapping up this week. The wood material for the floor arrives this week and the RTUs will be on.
- Our goal to have the building envelope in place by Thanksgiving is in jeopardy, but we're close!

Overall Building – 10/26/17






Building from Northeast – 10/26/17 (Above) & from the Southwest (Below)





Roof Structure / Commons Overbuild (Above) & South Mechanical Well (Below)



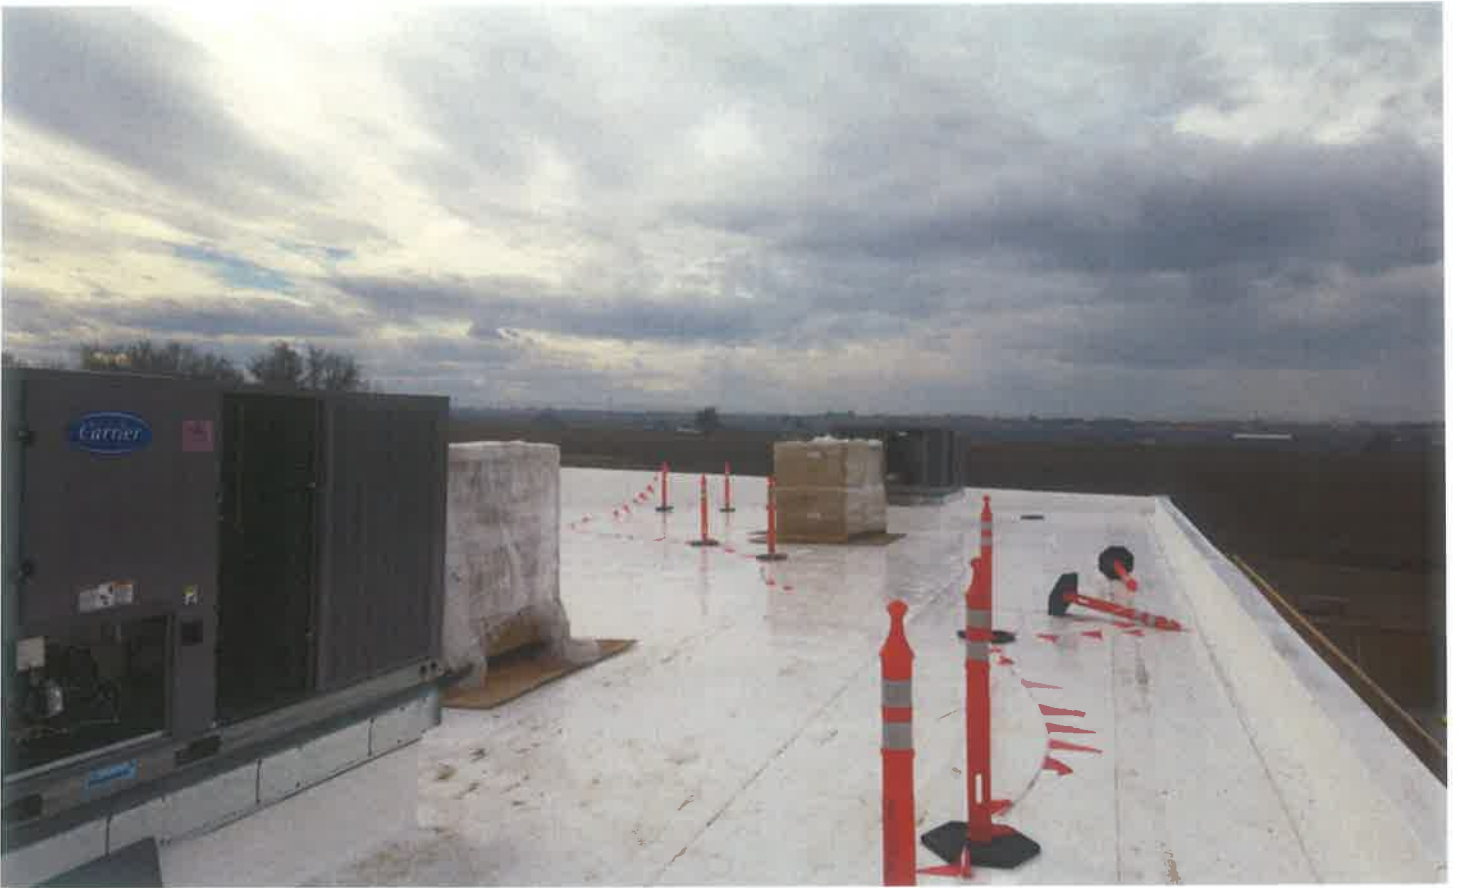

Gym RTU's (Above) & Gym Interior (Below)





North Elevation Set-Up for Veneer (Above) & East Overhang (Below)





Classroom Window Wall (Above) & Classroom Rough-In Work (Below)

